


ID	Task Mode	Task Name	Duration	Scheduled Start	Scheduled Finish	ASUFGSD Transportation Facility
1		Permitting	174 days	Mon 2/21/22	Thu 10/20/22	
2		Civil Permit Received	23 days	Mon 2/21/22	Wed 3/23/22	
3		Building Permit Received	1 day	Mon 2/21/22	Mon 2/21/22	
4		Off-site Permit Received	1 day	Tue 3/8/22	Tue 3/8/22	
5		Mobilization	8 days	Wed 3/23/22	Wed 3/23/22	
6		Fencing	1 day	Wed 3/23/22	Thu 3/3/22	
7		Job Trailer	1 day	Fri 2/25/22	Wed 3/23/22	
8		Tractor SWPP	3 days	Tue 2/22/22	Fri 2/25/22	
9		Trailer Power	1 day	Mon 2/28/22	Mon 2/28/22	
10		Site Signage	1 day	Thu 3/3/22	Thu 3/3/22	
11		Cut Opening in Fence	2 days	Mon 2/28/22	Tue 3/1/22	
12		Locate Existing Utilities	1 day	Tue 2/22/22	Tue 2/22/22	
13		Site Work/ Civil	87 days	Wed 2/23/22	Thu 6/23/22	
14		Survey	2 days	Wed 2/23/22	Thu 2/24/22	
15		Mobilize	1 day	Fri 2/25/22	Fri 2/25/22	
16		On-site Demo	1 day	Fri 2/25/22	Fri 2/25/22	
17		Clear/grub 4'	2 days	Mon 2/28/22	Tue 3/1/22	
18		Export Dirt	2 days	Fri 3/25/22	Fri 3/25/22	
19		Fire Lane Access	2 days	Thu 3/24/22	Fri 3/25/22	
20		Build Up Building Pad	4 days	Wed 3/2/22	Mon 3/7/22	
21		Retention Basin Grading	2 days	Tue 3/8/22	Wed 3/9/22	
22		Certify Pad	1 day	Tue 3/8/22	Tue 3/8/22	
23		Parking Lot Grading	10 days	Thu 3/10/22	Wed 3/23/22	
24		On Site Light Pole Bases	5 days	Thu 3/24/22	Wed 3/30/22	
25		Parking lot aggregate	5 days	Thu 5/12/22	Wed 5/18/22	
26		Lay Asphalt	4 days	Tue 5/19/22	Tue 5/24/22	
27		Form Curb & Gutter	10 days	Thu 3/24/22	Wed 4/6/22	
28		Pour Curb & Gutter	5 days	Thu 4/7/22	Wed 4/13/22	
29		Form Sidewalk	15 days	Thu 4/14/22	Wed 5/4/22	
30		Pour sidewalk	15 days	Mon 5/9/22	Fri 5/27/22	
31		Truck Dock / Trash Enclosure Foundation	5 days	Thu 3/31/22	Wed 4/6/22	
32		Pour Truck Dock/ Trash Enclosure	2 days	Mon 4/11/22	Tue 4/12/22	
33		Paint CMU	1 day	Mon 4/11/22	Mon 4/11/22	
34		Repair Landscape	5 days	Mon 5/30/22	Fri 6/3/22	
35		Install Chain Link Fence	10 days	Mon 5/30/22	Fri 6/10/22	
36		Gates	4 days	Mon 6/13/22	Thu 6/16/22	
37		Gate Power/access control	5 days	Fri 6/17/22	Thu 6/23/22	
38		Striping/Signage	2 days	Thu 4/7/22	Fri 4/1/22	
39		Site Work Complete	2 days	Wed 6/8/22	Thu 6/9/22	
40		Offsite Civil	90 days	Fri 6/10/22	Mon 6/13/22	
41		Construction Signage/ Traffic Control Plan	3 days	Thu 3/24/22	Wed 7/27/22	
42		Sawcut existing asphalt/concrete	3 days	Thu 3/29/22	Thu 3/31/22	
43		New Utilities	10 days	Fri 4/1/22	Thu 4/14/22	
44		Relocate existing Utilities	10 days	Fri 4/15/22	Thu 4/28/22	
45		Relocate existing Irrigation/landscape	5 days	Fri 4/29/22	Thu 5/5/22	
46		Traffic signal/ comm wire	5 days	Fri 5/6/22	Thu 5/12/22	
47		Connect to storm drain	5 days	Fri 4/29/22	Thu 5/5/22	
48		Form Curb/gutter/sidewalk	20 days	Fri 5/6/22	Thu 5/12/22	
49		Pour Curb/gutter/sidewalk	3 days	Tue 5/10/22	Mon 6/6/22	
50		Form bullnose	4 days	Tue 6/7/22	Thu 6/9/22	
51		Pour Bullnose	4 days	Fri 6/10/22	Wed 6/15/22	
52		Aggregate Base	5 days	Thu 4/7/22	Tue 4/12/22	
53		Lay asphalt entrance	3 days	Thu 6/16/22	Wed 6/22/22	
54		Striping / Signage	1 day	Thu 6/23/22	Mon 6/27/22	
55		Off-site Work Complete	1 day	Tue 7/26/22	Wed 7/27/22	
56		Stormwater	18 days	Thu 3/10/22	Mon 4/4/22	
57		Grouted Rip-Rap	10 days	Tue 3/22/22	Mon 4/4/22	
58		Storm/french Drain	5 days	Thu 3/24/22	Wed 3/30/22	
59		Catch basin	3 days	Thu 3/17/22	Mon 3/21/22	
60		Drywell	4 days	Thu 3/10/22	Tue 3/15/22	

# Schedule

Due to Ci traffic c

Site Work/ Civil

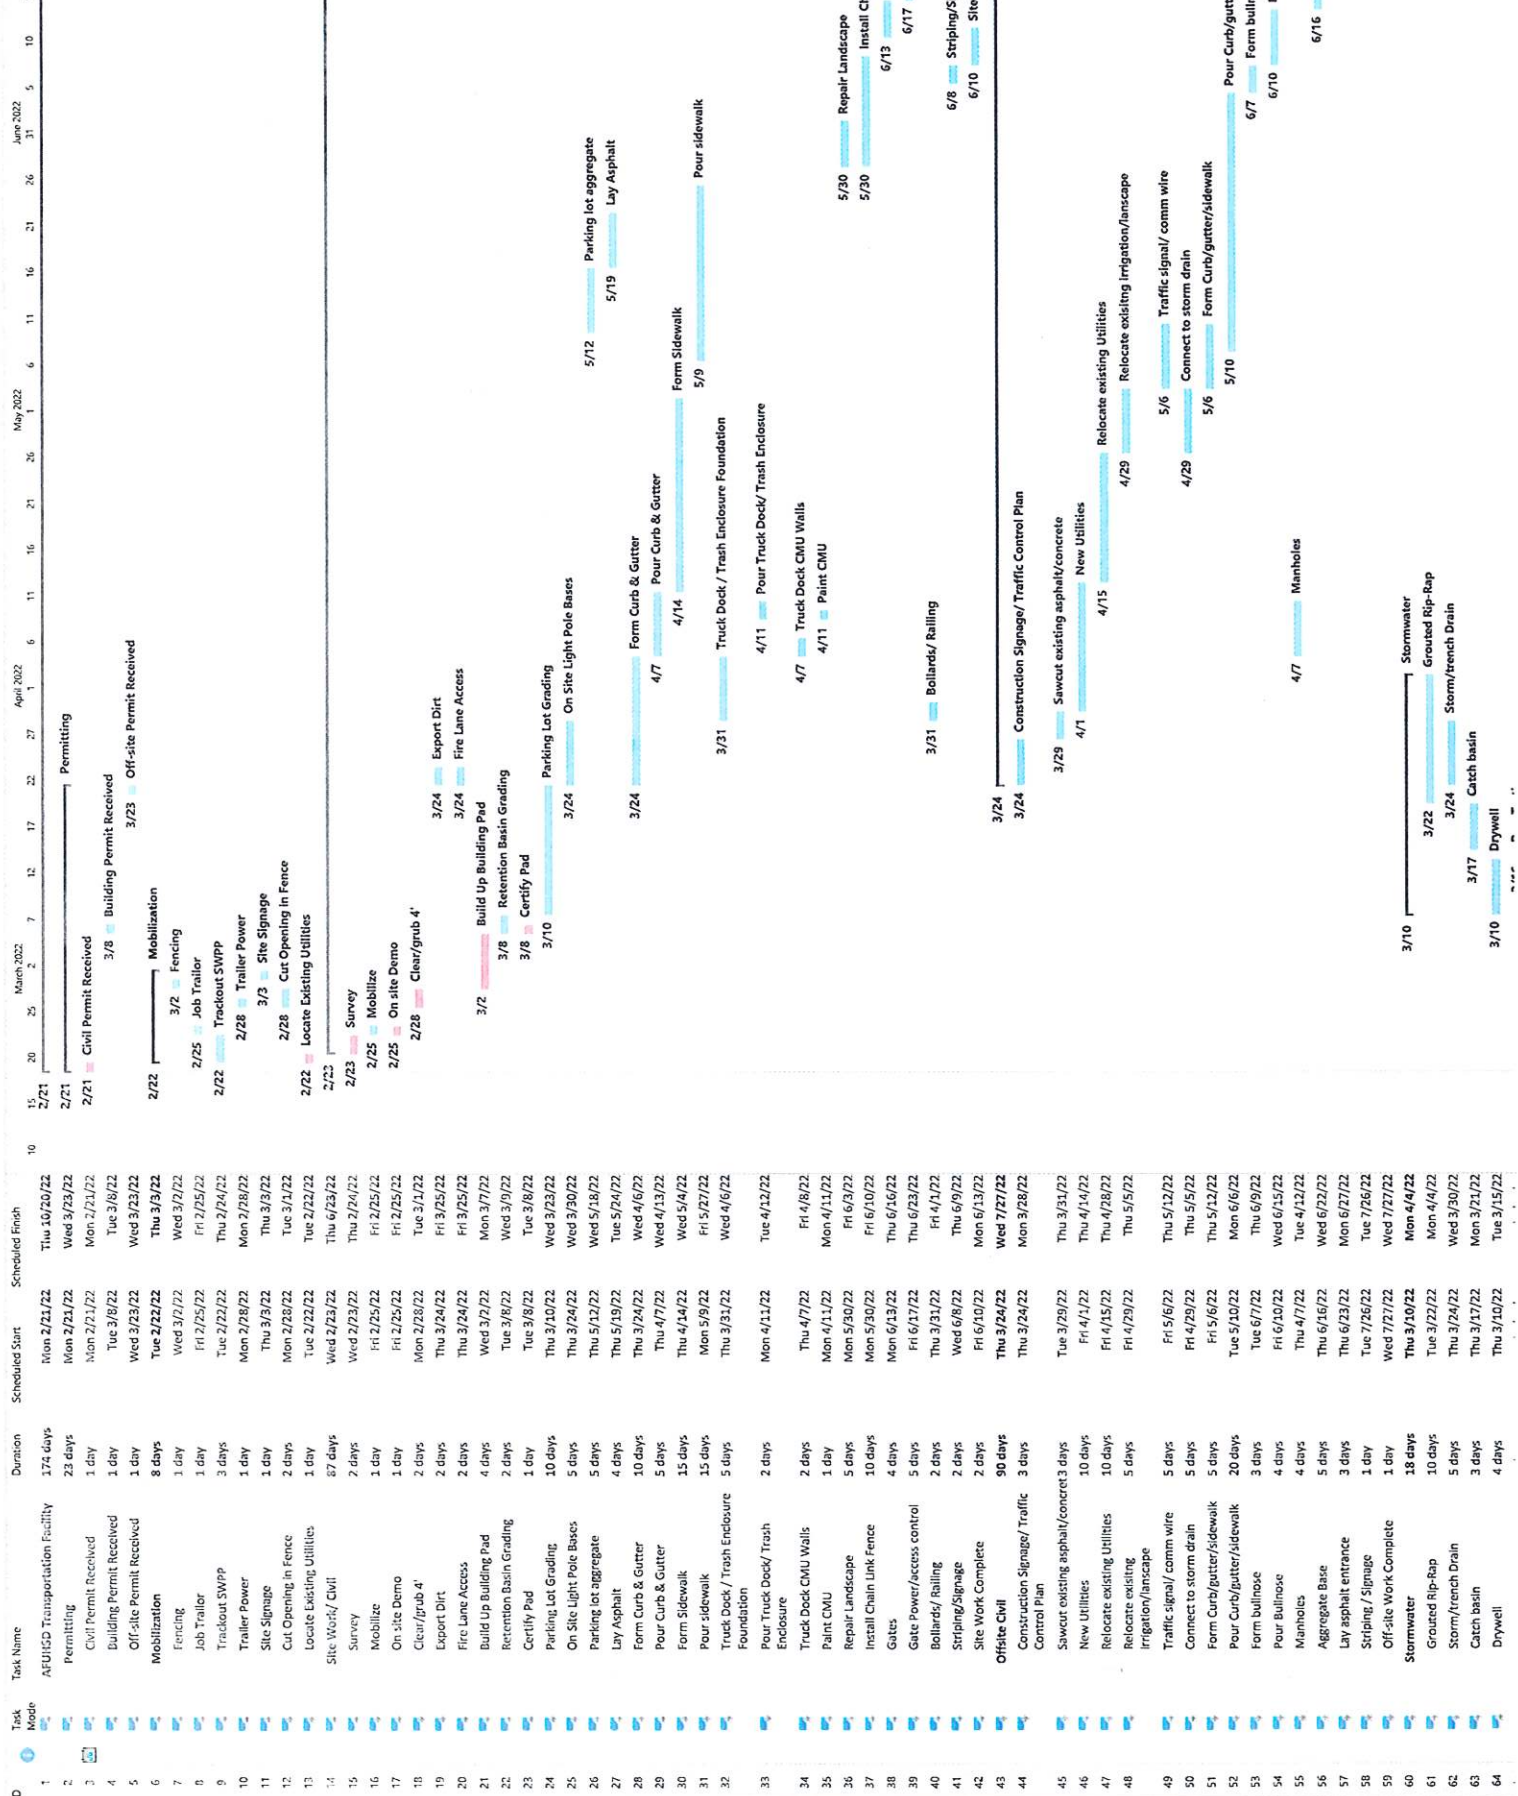

ID	Task Mode	Task Name	Duration	Scheduled Start	Scheduled Finish
79	Power	Power	62 days	Wed 3/9/22	Thu 6/2/22
80	Approved APS Drawings	Approved APS Drawings	40 days	Wed 3/9/22	Tue 5/3/22
81	APS Power Coordination Meeting	APS Power Coordination Meeting	5 days	Wed 5/4/22	Tue 5/10/22
82	Trenching for Conduit	Trenching for Conduit	3 days	Fri 5/11/22	Fri 5/13/22
83	Primary Conduit	Primary Conduit	3 days	Mon 5/16/22	Wed 5/18/22
84	Secondary Conduit	Secondary Conduit	4 days	Thu 5/19/22	Tue 5/24/22
85	Inspections / Backfill	Inspections / Backfill	5 days	Tue 5/17/22	Mon 5/23/22
86	Transformer Pad	Transformer Pad	2 days	Tue 5/24/22	Wed 5/25/22
87	Set Transformer	Set Transformer	1 day	Thu 6/2/22	Thu 6/2/22
88	Foundation	Foundation	30 days	Wed 3/9/22	Tue 4/19/22
89	Plumbing Underground	Plumbing Underground	8 days	Wed 3/9/22	Fri 3/18/22
90	Electrical Underground	Electrical Underground	10 days	Mon 3/21/22	Fri 4/1/22
91	Dig Footings	Dig Footings	2 days	Wed 3/16/22	Thu 3/17/22
92	Rebar at Footings	Rebar at Footings	2 days	Thu 3/17/22	Fri 3/18/22
93	Pour Footings	Pour Footings	3 days	Mon 3/21/22	Wed 3/23/22
94	Pad ABC	Pad ABC	5 days	Mon 4/4/22	Fri 4/8/22
95	Vapor Barrier	Vapor Barrier	2 days	Mon 4/11/22	Tue 4/12/22
96	Rebar at Pad	Rebar at Pad	6 days	Mon 4/11/22	Mon 4/18/22
97	Pour Slab	Pour Slab	3 days	Fri 4/15/22	Tue 4/19/22
98	Fuel Equipment	Fuel Equipment	36 days	Tue 4/12/22	Tue 5/31/22
99	Trench for below ground Fuel Pipe	Trench for below ground Fuel Pipe	2 days	Tue 4/12/22	Wed 4/13/22
100	Run Below ground pipe	Run Below ground pipe	4 days	Thu 4/14/22	Tue 4/19/22
101	Trench for underground electrical	Trench for underground electrical	1 day	Wed 4/20/22	Wed 4/20/22
102	Conduit for electrical/low voltage	Conduit for electrical/low voltage	2 days	Thu 4/21/22	Fri 4/22/22
103	Backfill/grading	Backfill/grading	3 days	Mon 4/25/22	Wed 4/27/22
104	Forms for tank pad/island	Forms for tank pad/island	2 days	Fri 5/6/22	Mon 5/9/22
105	Light Pole Bases	Light Pole Bases	3 days	Thu 4/28/22	Mon 5/2/22
106	Pour tank pad/island	Pour tank pad/island	1 day	Tue 5/10/22	Tue 5/10/22
107	Set equipment	Set equipment	2 days	Wed 5/18/22	Thu 5/19/22
108	SES Panel	SES Panel	2 days	Fri 5/20/22	Mon 5/23/22
109	Set Bollards	Set Bollards	3 days	Tue 5/3/22	Thu 5/5/22
110	Run power/low voltage	Run power/low voltage	5 days	Tue 5/24/22	Mon 5/30/22
111	Final Grading	Final Grading	1 day	Tue 5/31/22	Tue 5/31/22
112	Striping/Signage	Striping/Signage	1 day	Wed 5/11/22	Wed 5/11/22
113	Building Exterior	Building Exterior	106 days	Tue 3/29/22	Tue 8/23/22
114	Warehouse / Service	Warehouse / Service	104 days	Tue 3/29/22	Fri 8/19/22
115	Stems	Stems	4 days	Tue 3/29/22	Fri 4/1/22
116	CMU Walls	CMU Walls	25 days	Wed 4/27/22	Tue 5/31/22
117	Set embeds	Set embeds	3 days	Wed 5/18/22	Fri 5/20/22
118	Lintels	Lintels	2 days	Tue 5/17/22	Wed 5/18/22
119	Steel Columns	Steel Columns	2 days	Wed 6/1/22	Thu 6/2/22
120	Steel Joists	Steel Joists	2 days	Fri 6/3/22	Mon 6/6/22
121	Steel Detailing/ Roof frames	Steel Detailing/ Roof frames	3 days	Tue 6/7/22	Thu 6/9/22
122	Steel Decking	Steel Decking	3 days	Fri 6/10/22	Tue 6/14/22
123	Exhaust & Vent Penetrations	Exhaust & Vent Penetrations	1 day	Wed 6/15/22	Wed 6/15/22
124	HVAC curbs/ Penetrations	HVAC curbs/ Penetrations	2 days	Wed 6/15/22	Thu 6/16/22
125	Electrical Roof Penetrations	Electrical Roof Penetrations	3 days	Fri 6/17/22	Tue 6/21/22
126	Metal Roof Accessories	Metal Roof Accessories	4 days	Fri 7/1/22	Wed 7/6/22
127	Roofing	Roofing	7 days	Wed 6/22/22	Thu 6/30/22
128	Powerwash CMU	Powerwash CMU	5 days	Fri 7/1/22	Thu 7/7/22
129	Overhead Doors	Overhead Doors	5 days	Fri 7/8/22	Thu 7/14/22
130	Metal Doors	Metal Doors	5 days	Fri 7/15/22	Thu 7/21/22
131	Exterior Paint	Exterior Paint	10 days	Tue 8/2/22	Mon 8/15/22
132	Windows	Windows	2 days	Fri 7/22/22	Mon 7/25/22
133	Mechanical Louvers	Mechanical Louvers	5 days	Tue 7/26/22	Mon 8/1/22
134	Exterior Lighting	Exterior Lighting	3 days	Tue 8/16/22	Thu 8/18/22
135	Building Exterior Complete	Building Exterior Complete	1 day	Fri 8/19/22	Fri 8/19/22
136	Admin	Admin	102 days	Mon 4/4/22	Tue 8/23/22
137	Stems	Stems	3 days	Mon 4/4/22	Wed 4/6/22
138	CMU Walls	CMU Walls	7 days	Wed 6/1/22	Thu 6/9/22
139	Set Embeds	Set Embeds	2 days	Mon 6/6/22	Tue 6/7/22



ID	Task Name	Duration	Scheduled Start	Scheduled Finish
154	Exterior Paint	3 days	Tue 6/16/22	Thu 8/18/22
155	Exterior Lighting	3 days	Fri 8/19/22	Tue 8/23/22
156	Storefront Doors	3 days	Wed 7/13/22	Fri 7/15/22
157	Windows	3 days	Mon 7/11/22	Wed 7/13/22
158	Building Interior	66 days	Mon 7/11/22	Mon 10/10/22
159	Warehouse/Service	24 days	Mon 7/11/22	Thu 8/11/22
160	Paint exposed steel	2 days	Mon 7/11/22	Tue 7/12/22
161	Fire Sprinkler Rough	4 days	Wed 7/13/22	Mon 7/18/22
162	Mechanical Rough-in	5 days	Wed 7/13/22	Tue 7/19/22
163	Electrical Rough-in	10 days	Wed 7/13/22	Tue 7/26/22
164	Plumbing Rough-in	5 days	Wed 7/13/22	Tue 7/19/22
165	Data Rough-in	4 days	Wed 7/27/22	Mon 8/1/22
166	Fan Install	2 days	Wed 7/27/22	Thu 7/28/22
167	Heater Install	5 days	Wed 7/27/22	Tue 8/2/22
168	Light Install	5 days	Wed 7/27/22	Tue 8/2/22
169	Concrete Floor Scaler	2 days	Wed 8/3/22	Thu 8/4/22
170	Equipment Install	4 days	Fri 8/5/22	Wed 8/10/22
171	Door Hardware	3 days	Wed 7/13/22	Fri 7/15/22
172	Signage	1 day	Thu 8/11/22	Thu 8/11/22
173	Admin	64 days	Wed 7/13/22	Mon 10/10/22
174	Paint exposed steel	1 day	Wed 7/13/22	Wed 7/13/22
175	Fire Sprinkler Rough-in	3 days	Thu 7/14/22	Mon 7/18/22
176	Framing	5 days	Mon 7/18/22	Fri 7/22/22
177	Rigid Insulation	1 day	Mon 7/25/22	Mon 7/25/22
178	Mechanical Insulation	5 days	Mon 8/1/22	Fri 8/5/22
179	Electrical Rough-in	10 days	Mon 7/25/22	Fri 8/5/22
180	Plumbing Rough-in	5 days	Mon 7/25/22	Fri 7/29/22
181	Data Rough-in	5 days	Mon 7/25/22	Fri 7/29/22
182	Electrical Ceiling Rough	5 days	Mon 8/8/22	Fri 8/12/22
183	Mechanical Ceiling Rough	5 days	Mon 7/25/22	Fri 7/29/22
184	Buckling	1 day	Mon 8/15/22	Mon 8/15/22
185	Wall Insulation	3 days	Tue 8/16/22	Thu 8/18/22
186	Hang Drywall	9 days	Fri 8/19/22	Wed 8/31/22
187	Hang Doors	4 days	Fri 9/16/22	Wed 9/21/22
188	Ceiling Grid	3 days	Fri 9/16/22	Tue 9/20/22
189	Hang Ceiling	1 day	Thu 9/1/22	Thu 9/1/22
190	Tap and Texture	6 days	Fri 9/2/22	Fri 9/9/22
191	Paint	4 days	Mon 9/12/22	Thu 9/15/22
192	Millwork	7 days	Fri 9/16/22	Mon 9/26/22
193	Electrical Trim	5 days	Fri 9/16/22	Thu 9/22/22
194	Plumbing Trim	5 days	Mon 9/12/22	Fri 9/16/22
195	Mechanical Trim	2 days	Wed 9/21/22	Thu 9/22/22
196	Partitions	2 days	Mon 9/19/22	Tue 9/20/22
197	Flooring	10 days	Fri 9/23/22	Thu 10/6/22
198	Wall Tile	7 days	Thu 9/1/22	Fri 9/9/22
199	Accessories	2 days	Wed 9/21/22	Thu 9/22/22
200	Door Hardware	4 days	Fri 9/16/22	Wed 9/21/22
201	Signage	2 days	Fri 9/16/22	Mon 9/19/22
202	Rough Cican	2 days	Fri 10/7/22	Mon 10/10/22
203	Landscaping	50 days	Tue 5/3/22	Mon 7/11/22
204	Irrigation	32 days	Tue 5/3/22	Wed 6/15/22
205	Coordinate install meter/backflow	2 days	Tue 5/3/22	Wed 5/4/22
206	Guardshack Enclosure	1 day	Mon 5/9/22	Mon 5/9/22
207	Trenching for Irrigation Lines	2 days	Fri 6/10/22	Mon 6/13/22
208	Irrigation Main w/ sleeving	4 days	Wed 6/8/22	Mon 6/13/22
209	Install valves and boxes	1 day	Tue 6/14/22	Tue 6/14/22
210	Install emitter	1 day	Wed 6/15/22	Wed 6/15/22
211	Mount control box / coordinate power and low voltage	1 day	Wed 6/15/22	Wed 6/15/22
212	Planting / Final Grading	19 days	Wed 6/15/22	Mon 7/11/22
213	Swales	3 days	Wed 6/15/22	Fri 6/17/22
214	Plant trees	6 days	Mon 6/20/22	Mon 6/27/22
215	Plant shrubs	3 days	Tue 6/28/22	Thu 6/30/22
216	Plants	1 day	Fri 7/1/22	Fri 7/1/22

